ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			NTP	5 days	Mon 2/24/25	Fri 2/28/25	
2			Mobilization	5 days	Mon 2/24/25	Fri 2/28/25	1SS
3	✓		Survey	20 days	Mon 3/3/25	Fri 3/28/25	2
4	✓		Pothole	20 days	Mon 3/3/25	Fri 3/28/25	2
5			**Ironhorse**	**320 days**	**Mon 3/3/25**	**Fri 5/22/26**	
6	✓		Video Assesment	60 days	Mon 3/3/25	Fri 5/23/25	2
7			CO's and Wye Connections	270 days	Mon 5/12/25	Fri 5/22/26	6SS+50 days
8			Mainline Lining	215 days	Mon 4/14/25	Fri 2/6/26	
9			Lateral Lining/Cleanouts	250 days	Mon 6/9/25	Fri 5/22/26	7SS+20 days,6
10	✓		Pumpstation Tree Removal	3 days	Tue 3/25/25	Thu 3/27/25	2
11	✓		Nantucket Bypass Pumping	25 days	Mon 4/7/25	Fri 5/9/25	4FS+5 days
12	✓		Nantucket MH's and Gravity Sewer	20 days	Mon 4/14/25	Fri 5/9/25	
13			**Lift Station**	**56 days**	**Mon 7/21/25**	**Mon 10/6/25**	
14	✓		Excavate/Shore for Lift Station	4 days	Mon 7/21/25	Thu 7/24/25	34
15	✓		Prep Base/Install Sections	2 days	Fri 7/25/25	Mon 7/28/25	14
16	✓		Core Drill	2 days	Tue 7/29/25	Wed 7/30/25	15
17	✓		36" Pipe Stub and Cleanout	7 days	Thu 8/14/25	Fri 8/22/25	16,21
18	✓		Layout/Install Pump Rails & Bases	3 days	Thu 7/31/25	Mon 8/4/25	16
19	✓		Interior Mechanical Piping	3 days	Tue 8/5/25	Thu 8/7/25	18
20	✓		4" Vertical Discharge Piping	2 days	Fri 8/8/25	Mon 8/11/25	19
21	✓		Backfill to 4" Discharge Invert	2 days	Tue 8/12/25	Wed 8/13/25	20
22	✓		Excavate/Prep for Vault	2 days	Thu 8/14/25	Fri 8/15/25	21
23	✓		Install New Vault	2 days	Mon 8/18/25	Tue 8/19/25	22
24	✓		4" Discharge Piping Through Vault	4 days	Wed 8/20/25	Mon 8/25/25	23
25	✓		Grout Lift Station and Vault	4 days	Tue 8/26/25	Fri 8/29/25	24
26	✓		Backill Lift Station and Vault	3 days	Tue 8/26/25	Thu 8/28/25	24
27			Electrical	25 days	Fri 8/29/25	Thu 10/2/25	26
28			Start Up/Testing	2 days	Fri 10/3/25	Mon 10/6/25	27
29			48" Manhole Replacement	14 days	Thu 9/18/25	Tue 10/7/25	12,31
30			60" Manhole	3 days	Mon 8/25/25	Wed 8/27/25	17
31			Gravity Sewer	15 days	Thu 8/28/25	Wed 9/17/25	30
32	✓		Manhole Rehab	50 days	Mon 5/26/25	Fri 8/1/25	8SS+30 days
33	✓		6" HDPE Forcemain	23 days	Mon 6/9/25	Wed 7/9/25	
34	✓		Pressure Sewer Service Valve Assembly	25 days	Mon 6/16/25	Fri 7/18/25	33SS+5 days
35			Install E-One Pumpstations	75 days	Tue 9/16/25	Mon 12/29/25	34,26,38SS+10 da
36			E-One Electrical	70 days	Tue 9/30/25	Mon 1/5/26	38SS+15 days,35S
37			E-One Startup/Testing	28 days	Tue 1/6/26	Thu 2/12/26	36,28
38			Directional Drilling	31 days	Tue 9/2/25	Tue 10/14/25	34FS+12 days
39			4" Clean Outs/Side Service	140 days	Tue 9/16/25	Mon 3/30/26	35SS
40			1.5" Side Sewer Connections	140 days	Tue 9/16/25	Mon 3/30/26	39SS
41			Landscape Restoration	60 days	Tue 1/6/26	Mon 3/30/26	35FS-20 days,36
42			Gravel Driveway Restoration	10 days	Wed 10/29/25	Tue 11/11/25	43
43			Asphalt Patching/Paving	10 days	Wed 10/15/25	Tue 10/28/25	38
44			Final Completion	0 days	Fri 5/22/26	Fri 5/22/26	40,41,37,9,7,39

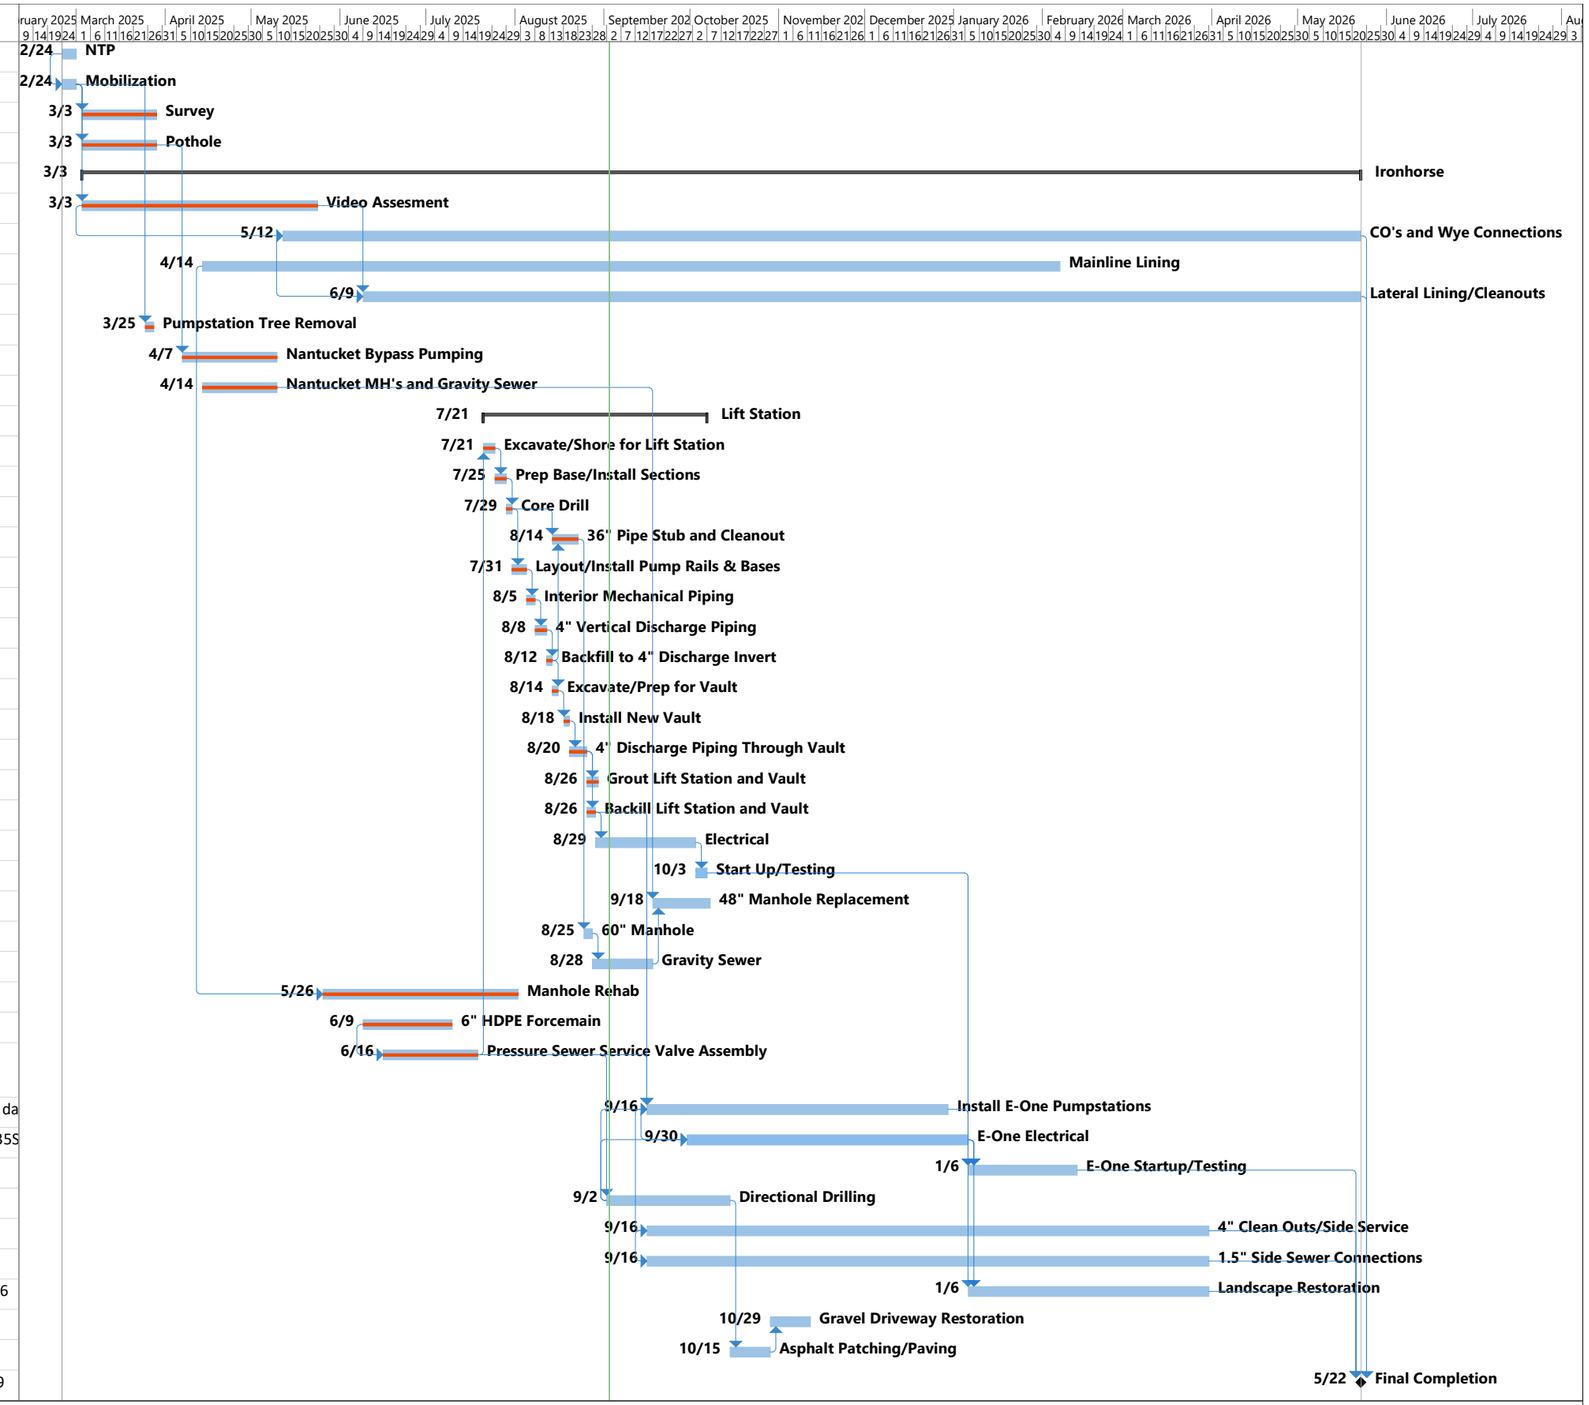

Project: Harstene Island Sewer -
Date: Wed 9/3/25

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			
